

DALLAS ISD 2008 BOND PROGRAM MONTHLY AT-A-GLANCE REPORT

CONSTRUCTION SERVICES - JULY 31, 2016



INTRODUCTION

The 2008 Dallas ISD Bond Program approved by Dallas voters in May 2008, started with the first sale of bonds in December 2008, and currently includes **252** CSP projects grouped into four program phases. The completion of construction is targeted in 2016. Three Program Management firms, AECOM, Jacobs and Parsons (PMs) assist the Construction Services staff with the management of the \$1.35 Billion program.

Summary By Project Type & Phase	No. of Projects			
	Phase 1	Phase 2	Phase 3	Phase 4
No. of New Construction:	5	5	3	1
No. of Addition / Renovations:	5	4	4	2
No. of Expansion / Renovations:	9	7	1	0
No. of Renovations:	80	73	45	8
Total No. of Projects by Phase	99	89	53	11
Total No. of Projects	252			
Total No. of Bid Packages by Phase	36	33	29	9

SCOPE

Project types consist of New Construction, Additions/Renovations, Expansion/Renovations and straight Renovations. School campuses, athletic and non-instructional facilities will receive improvements.

PROCUREMENT

Professional services procured to date include Program Managers and all consultants that support the design effort such as Architect/Engineers, Land Surveyors, Geotechnical, Geothermal, HazMat, Roofing, HVAC Controls, Test & Balance and other specialty consultants. In terms of procurement of construction services, **251** contractors have received Notices to Proceed (NTPs) to date.

PROGRESS

Out of the **252** total projects, **250** projects have reached substantial completion, including all phase 1, 2 and 3 projects and **nine** phase 4 projects. **248** projects have general contractors contracts closed. The close out of contracts for A/E firms and other vendors is also progressing. Phase 4 has **1** project in the design phase, **1** project in the construction phase and **9** projects substantially complete or closed.

By Project Stage	No. of Projects			
	Phase 1	Phase 2	Phase 3	Phase 4
Pre-Design (STB)	✓	✓	✓	1
Schematic Design	✓	✓	✓	0
Design Development	✓	✓	✓	0
Construction Documents	✓	✓	✓	0
Procurement / Bidding / NTP Issued	✓	✓	✓	0
In Construction	✓	✓	✓	1
Substantial Completion	✓	✓	✓	2
Closed	✓	✓	✓	7

SAFETY

Construction safety is priority one for the District. Consultants, vendors and contractors must have successfully passed the strict background checks and drug testing program to maintain active ID badges.


SCHEDULE

The overall program and all phases are on target to meet adjusted milestones.

PROGRAM TIMELINE									
2009	2010	2011	2012	2013	2014	2015	2016	2017	2018
Phase 1									
	Phase 2								
		Phase 3							
				Phase 4					

BUDGET

The overall budget managed for the 2008 Dallas ISD Bond Program is **\$1,338,437,376** inclusive of funds for construction and technology. To date, **97%** of the budget has been committed via multiple contracts and **96%** has been paid. Overall the program is within budget.

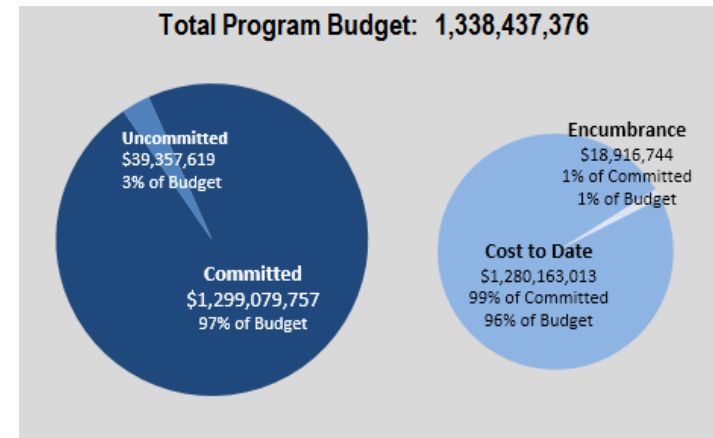

Note: At the March 26, 2015 Board Meeting, the Dallas ISD Board of Trustees approved the 'Interim Bridge Plan'. The work will include re-opening and/or re-purposing schools, renovating and/or making additions to address critical needs and expanding pre-kindergarten spaces. The total approved funds of \$148,000,000 were from the following sources: 2008 Bond Program Funds (\$30,000,000), Maintenance Tax Notes (\$75,000,000) and Dallas ISD General Operating Funds (\$43,000,000). Details for the projects added from the Interim Bridge Plan are shown on the '2015 Interim Bridge Plan Monthly Report'.

M/WBE UTILIZATION

The M/WBE Program is based on the principle of creating and providing opportunities for M/WBE vendors. The M/WBE Program, through the Board of Trustees policy, promotes JV partnerships with certified M/WBE firms, beyond traditional subcontracting opportunities. The M/WBE utilization goals established for the Program by the Board of Trustees are: 35% for professional and other services and 30% for construction services. All services are on target to exceed the goals.
