

# 2008 DALLAS ISD BOND PROGRAM AT A GLANCE

## CONSTRUCTION SERVICES

### OCTOBER 31, 2012



The 2008 Dallas ISD Bond Program approved by Dallas voters in May 2008, started with the first sale of bonds in December 2008, and includes 223 projects grouped into three program phases. The completion of construction is targeted in 2014. Three Program Management firms, AECOM, Jacobs and Parsons (PMs) assist the Construction Services staff with the management of the \$1.35 Billion program.

### SCOPE

Project types consist of New Construction, Additions/Renovations, Expansion/Renovations and straight Renovations. School campuses, athletic and non-instructional facilities will receive improvements.

Participation of minority- and women-owned businesses in Dallas ISD's bond-funded projects exceeded district goals in the fourth quarter of fiscal year 2011-2012, according to a report presented to the Board of Trustees. For construction projects in the 2008 Bond Program, 59 percent (\$21.6 million) of construction work was completed by M/WBE companies between April 1 and June 30, 2012, during which \$36.4 million was spent on bond projects for construction. During the same period, 57 percent (\$5.8 million) of professional services relating to the 2008 Bond Program were provided by M/WBE firms, during which \$10.1 million was spent on bond professional services. The participation in both categories exceeds the district's M/WBE goals, which are 30 percent for construction and 35 percent for professional services.

Summary By Project Type & Phase	No. of Projects		
	Ph 1	Ph 2	Ph 3
No. of New Construction:	5	5	4
No. of Addition / Renovations:	5	4	4
No. of Expansion / Renovations:	9	7	1
No. of Renovations:	80	69	30
Total No. of Projects by Phase	99	85	39
Total No. of Projects	223		
Total No. of Bid Packages	91		

### PROCUREMENT

Professional services procured to date include Program Managers and all consultants that support the design effort such as Architect/Engineers, Land Surveyors, Geotechnical, Geothermal, HazMat, Roofing, HVAC Controls, Test & Balance and other specialty consultants. In terms of procurement of construction services, 211 projects have received Notices to Proceed (NTPs) to date.

By Project Stage	No. of Projects		
	Phase 1	Phase 2	Phase 3
Started	✓	✓	✓
Pre-Design (STB)	✓	✓	1
Schematic Design	✓	✓	0
Design Development	✓	✓	0
Construction Documents	✓	✓	0
Procurement / Bidding / NTP Issued	✓	✓	11
In Construction	5	9	26
Substantial Completion	2	24	1
Closed	92	52	0

### PROGRESS

222 Phase 1, 2 & 3 projects have completed the design phase at this time. 171 projects have reached substantial completion, including 76 projects in phase 2 and 1 project in phase 3. 144 projects have general contractors contracts closed. The close out of contracts for A/E firms and other vendors is also progressing. The design and procurement of Phase 3 projects is moving forward as planned. 11 projects are in the procurement and bidding process with 26 projects in construction.

✓ Indicates Stage completed


### SAFETY

Construction safety is priority one for the District. Consultants, vendors and contractors, who have successfully passed the strict background checks and drug testing program and maintain active ID badges total 7,077.

### SCHEDULE


The program timeline has been extended to accommodate new projects ongoing at multiple schools. Funded with savings generated by efficiencies in the administration of the program, these new projects expand the original scope of work and provide additional needed improvements. The overall program and all phases are on target to meet adjusted milestones.

#### PROGRAM TIMELINE



### BUDGET

The overall budget managed for the 2008 Dallas ISD Bond Program is \$1,365,746,934, inclusive of funds for construction and technology. To date, 82% of the budget has been committed via multiple contracts and 68% has been paid. Overall the program is within budget.

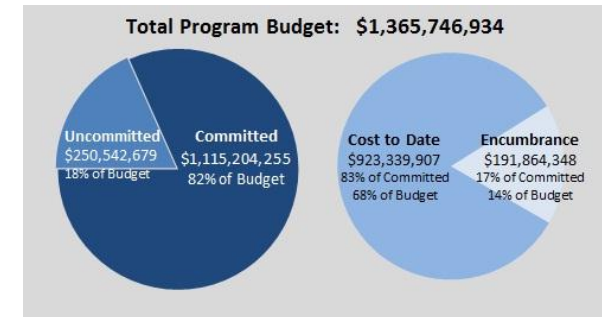

### M/WBE UTILIZATION

The M/WBE Program is based on the principle of creating and providing opportunities for M/WBE vendors. This year the Board of Trustees revised its policy to promote JV partnerships with certified M/WBE firms, beyond traditional subcontracting opportunities. The M/WBE utilization goals established for the Program by the Board of Trustees are: 35% for professional and other services and 30% for construction services. All services are on target to exceed the goals.

Dallas ISD officials, community leaders, students, and families gathered to celebrate the legacy of the late Gov. Ann Richards as they dedicated the new Ann Richards Middle School at 3831 N. Prairie Creek Rd on November 2, 2012. "A new school is a promise," said Dallas ISD Chief of School Leadership, Dr. Sylvia Reyna. "To the staff, it says we value you and want you to teach in a quality atmosphere. To the parents and community, it says we are committed to providing effective instruction so that every child can realize his or her dreams for the future. We thank the voters for the confidence they showed in Dallas ISD when they approved the bond program that created this new school." Throughout her lifetime, Texas Governor Ann Richards advocated equal rights for women and minorities. During her term as governor, she worked to improve Texas education.
