



2008 Dallas ISD Bond Program

Program Managers' Quarterly Summary Report

February 29, 2012



JACOBS

PARSONS


AECOM

PROGRAM MANAGERS' QUARTERLY SUMMARY REPORT

as of February 29, 2012

By Project Stage	No. of Projects		
	Phase 1	Phase 2	Phase 3
Started	✓	✓	✓
Pre-Design (STB)	✓	✓	5
Schematic Design	✓	✓	2
Design Development	✓	✓	8
Construction Documents	✓	✓	17
Procurement / Bidding / NTP Issued	✓	2	10
In Construction	13	52	0
Substantial Completion	19	33	0
Closed	67	2	0



% of Projects In/Completed by Phase & Stage

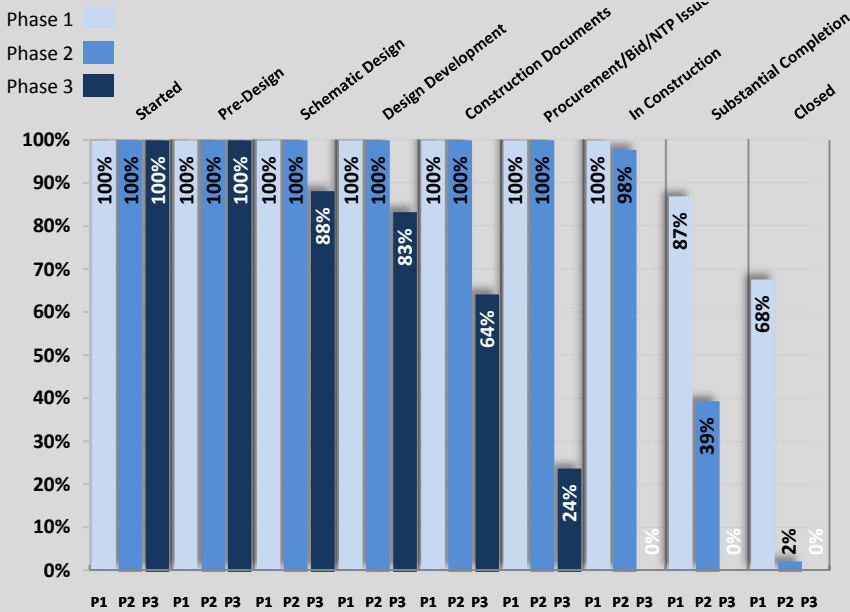

By Project Type	No. of Projects		
	Phase 1	Phase 2	Phase 3
No. of New Construction:	5	5	4
No. of Addition / Renovations:	5	4	4
No. of Expansion / Renovations:	9	7	1
No. of Renovations:	80	73	33
Total No. of Projects by Phase	99	89	42
Total No. of Projects	230		
Total No. of Bid Packages by Phase	36	33	22

Financial Summary

Total Program Budget: \$1,362,995,497

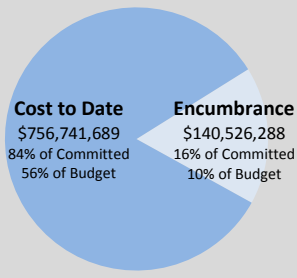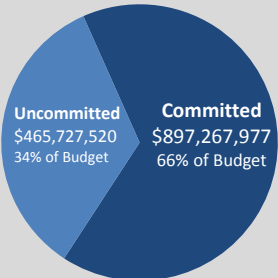

M/WBE Participation	Commitments to Date
PM Services (35% Goal):	46%
Professional Services (35% Goal):	38%
Construction (30% Goal):	37%

Time Line (New Schools)

	2009				2010				2011				2012				2013			
	O1	O2	O3	O4	O1	O2	O3	O4	O1	O2	O3	O4	O1	O2	O3	O4	O1	O2	O3	O4
2011 School Opening																				
George Herbert Walker Bush Elementary																				
Ebby Halliday Elementary																				
Kathlyn Joy Gilliam Collegiate Academy																				
2012 School Opening																				
Wilmer-Hutchins Elementary																				
Zan Wesley Holmes Jr. Middle School																				
W.H. Adamson High School																				
Balch Springs Middle School																				
Adelfa Botello Callejo Elementary																				
Ann Richards Middle School																				
Seagoville North Elementary																				
2013 School Opening																				
Jose "Joe" May Elementary																				
Billy Earl Dade Learning Center																				
Thelma Elizabeth Page Richardson Elementary																				
Oran M. Roberts Elementary																				



PROGRAM MANAGERS
AECOM
JACOBS
PARSONS



2008 Dallas ISD Bond Program
Exhibit A - Target Milestones - Phase 1
February 2012

Org No.	Project Name	Trustee District	Program Manager	Pre-Design (STB)	Schematic Design	Design Development	Construction Documents	Procurement - 1st Bid Ad	CSP Approval by Board	Estimated Construction NTP	Actual Construction NTP	Projected Substantial Completion	Actual Substantial Completion	Project Closeout
PHASE 1 PROJECTS														
001	Adams, Bryan HS	03	AECOM										5/20/2011	2/23/2012
101	Adams, John Q. ES	04	JACOBS										1/12/2011	6/23/2011
002	Adamson, W. H. HS	07	JACOBS									7/30/2012		
854	Alamo Pool	09	JACOBS										12/16/2011	
235	Alexander, Birdie ES	06	PARSONS										4/5/2011	1/26/2012
029	Alternative Placement Center at Village Fair	06	JACOBS										12/21/2010	8/25/2011
110	Blanton, Annie Webb ES	04	PARSONS										3/28/2011	10/20/2011
114	Bryan, John Neely ES	05	JACOBS										4/21/2011	9/22/2011
115	Budd, Harrell ES	05	PARSONS										5/5/2011	1/26/2012
304	Bush, George Herbert Walker ES	01	PARSONS										6/1/2011	
118	Bushman W. W. ES	05	JACOBS										3/29/2011	9/22/2011
120	Caillat, F.P. ES	01	PARSONS										10/1/2010	1/27/2011
122	Carr, C.F. ES	05	AECOM										11/3/2010	6/23/2011
124	Carver, George W. Learning Center	05	AECOM										12/29/2010	6/23/2011
130	Cowart, Leila P. ES	06	JACOBS										10/27/2010	2/24/2011
260	De Zavala, Lorenzo ES	07	AECOM										10/27/2010	5/26/2011
134	Dealey, George Bannerman Montessori School/Inter	01	PARSONS										10/5/2010	6/23/2011
135	DeGolyer, Everette L. ES	01	PARSONS										9/16/2010	1/27/2011
137	Dorsey, Julius ES	04	AECOM										11/12/2010	4/28/2011
144	Field, Tom W. ES	08	PARSONS										10/4/2010	2/24/2011
841	Forester, Herschel Stadium/Field House	04	AECOM										12/28/2010	5/26/2011
145	Foster, Stephen C. ES	01	PARSONS									5/29/2012		
842	Franklin Stadium	02	JACOBS									4/13/2012		
047	Franklin, Benjamin MS	02	PARSONS										12/7/2010	9/22/2011
048	Gaston, W.H. MS	03	AECOM										2/11/2011	6/23/2011
085	Gilliam, Kathlyn Joy Collegiate Academy	06	JACOBS										8/5/2011	
305	Halliday, Ebby ES	04	JACOBS										5/31/2011	10/20/2011
150	Hartlee, N. W. ES	05	JACOBS										3/21/2011	9/22/2011
156	Hawthorne, Nathaniel ES	04	JACOBS										1/7/2011	6/23/2011
152	Henderson, Margaret B. ES	07	JACOBS										10/28/2010	2/24/2011
153	Hexter, Victor H. ES	03	AECOM										5/10/2011	9/22/2011
006	Hillcrest HS	02	PARSONS										12/7/2010	9/22/2011
051	Holmes, Oliver Wendel MS	05	JACOBS										1/28/2011	9/22/2011
052	Hood, John B. MS	09	JACOBS										4/1/2011	8/25/2011
159	Hotchkiss, L.L. ES	03	AECOM									3/20/2012		
162	Jackson, Stonewall ES	02	AECOM									3/20/2012		
354	Kennedy-Curry MS	05	AECOM										7/13/2011	
166	Kiest, Edwin J. ES	03	AECOM										1/7/2011	4/28/2011
169	Kramer, Arthur ES	01	PARSONS										10/6/2010	6/23/2011
170	Lagow, Richard ES	04	PARSONS										3/25/2011	10/20/2011
171	Lakewood ES	02	AECOM									3/20/2012		
175	Lee, Umphrey ES	06	PARSONS										3/17/2011	1/26/2012
174	Lee, Robert E. ES	02	AECOM										6/7/2011	10/20/2011
177	Lipscomb, William ES	02	AECOM										6/13/2011	10/20/2011
851	Lisbon Pool	05	AECOM										10/29/2010	3/24/2011
849	Loos Pool	01	PARSONS										8/20/2010	1/27/2011
843	Loos, Alfred J. Athletic Complex	01	PARSONS										10/6/2011	



2008 Dallas ISD Bond Program
Exhibit A - Target Milestones - Phase 1
February 2012

Org No.	Project Name	Trustee District	Program Manager	Pre-Design (STB)	Schematic Design	Design Development	Construction Documents	Procurement - 1st Bid Ad	CSP Approval by Board	Estimated Construction NTP	Actual Construction NTP	Projected Substantial Completion	Actual Substantial Completion	Project Closeout
PHASE 1 PROJECTS														
856	Louis, Joe Field House at P.C. Cobb Athletic Comple	01	PARSONS										4/15/2011	
180	Macon, B.H. ES	04	AECOM										11/12/2010	4/28/2011
181	Maple Lawn ES	08	PARSONS									5/30/2012		
182	Marcus, Herbert ES	01	PARSONS										10/1/2010	1/27/2011
270	Mata, Eduardo ES	09	AECOM										6/3/2011	10/20/2011
185	Miller, William B. ES	05	JACOBS										3/28/2011	9/22/2011
186	Mills, Roger O. ES	05	JACOBS										12/14/2010	4/28/2011
187	Moseley, Nancy J. ES	04	PARSONS									3/24/2012		
188	Mount Auburn ES	08	AECOM										5/24/2011	11/17/2011
381	Obama, Barack Male Leadership Academy at B. F. D	05	JACOBS										10/6/2011	2/23/2012
193	Pershing, John J. ES	01	PARSONS										8/26/2010	1/27/2011
850	Pleasant Grove Pool	04	JACOBS										12/16/2011	
844	Pleasant Grove Stadium	04	JACOBS										11/17/2011	
194	Polk, K.B. Center for Academically Talented and Gift	02	PARSONS									5/31/2012		
195	Preston Hollow ES	02	PARSONS										10/6/2010	6/23/2011
198	Reilly, Marther Turner ES	03	AECOM										5/12/2011	9/22/2011
203	Rogers, Dan D. ES	03	AECOM									3/20/2012		
232	Rowe, Edna ES	09	AECOM										5/19/2011	9/22/2011
237	Runyon, John W. ES	04	PARSONS										2/25/2011	8/25/2011
055	Rusk, Thomas J. MS	08	PARSONS									5/28/2012		
205	Russell, Clinton P. ES	06	JACOBS										10/25/2011	
014	Samuell, W.W. HS	04	PARSONS										1/14/2011	5/26/2011
207	San Jacinto ES	09	AECOM										1/14/2011	6/23/2011
206	Sanger, Alex ES	03	AECOM										8/25/2011	12/15/2011
015	Seagoville HS	04	PARSONS										1/13/2012	
846	Seagoville Stadium	04	AECOM										1/20/2011	5/26/2011
249	Seguin, Erasmo Community Learning Center	06	JACOBS										10/25/2011	1/26/2012
262	Sequoyah Learning Center	05	AECOM										11/23/2010	8/25/2011
209	Silberstein, Ascher ES	09	AECOM										6/15/2011	1/26/2012
025	Skyline HS	09	AECOM										11/9/2011	
003	Smith, A. Maceo HS	05	JACOBS										10/13/2011	
845	Sprague Athletic Complex	06	AECOM										1/24/2011	5/26/2011
853	Sprague Pool	06	AECOM										10/29/2010	3/24/2011
017	Spruce, H. Grady HS	04	PARSONS										1/14/2011	5/26/2011
212	Stone, Harry Montessori Academy	05	JACOBS										12/29/2011	
141	Stone, Jill ES at Vickery Meadow	03	AECOM									3/20/2012		
060	Storey, Boude MS	06	PARSONS										3/31/2011	1/26/2012
213	Terry, T. G. ES	06	JACOBS										11/11/2010	6/23/2011
220	Twain, Mark Leadership Vanguard	06	PARSONS										3/17/2011	1/26/2012
222	Urban Park ES	04	AECOM										11/7/2011	
056	Walker, E.D. MS	01	PARSONS										1/27/2011	8/25/2011
225	Webster, Daniel ES	06	PARSONS										12/16/2011	
227	Wheatley, Phillis ES	09	AECOM										12/10/2010	5/26/2011
855	White Rock Pool	03	JACOBS									5/22/2012		
228	Williams, Sudie L. ES	02	PARSONS										10/20/2010	1/27/2011
301	Wilmer-Hutchins ES	05	PARSONS										1/19/2012	
380	Wilmer-Hutchins HS	05	JACOBS										11/29/2011	



2008 Dallas ISD Bond Program
Exhibit A - Target Milestones - Phase 1
February 2012

Org No.	Project Name	Trustee District	Program Manager	Pre-Design (STB)	Schematic Design	Design Development	Construction Documents	Procurement - 1st Bid Ad	CSP Approval by Board	Estimated Construction NTP	Actual Construction NTP	Projected Substantial Completion	Actual Substantial Completion	Project Closeout
PHASE 1 PROJECTS														
838	Wilmer-Hutchins Stadium	05	JACOBS										11/29/2011	
229	Winnetka ES	07	JACOBS										10/27/2010	2/24/2011
230	Withers, Harry C. ES	01	PARSONS										8/18/2010	1/27/2011
250	Young Jr., Whitney M. ES	05	JACOBS										11/17/2011	
072	Zumwalt, Sarah MS	05	JACOBS										12/9/2010	5/26/2011



2008 Dallas ISD Bond Program
Exhibit A - Target Milestones - Phase 2
February 2012

Org No.	Project Name	Trustee District	Program Manager	Pre-Design (STB)	Schematic Design	Design Development	Construction Documents	Procurement - 1st Bid Ad	CSP Approval by Board	Estimated Construction NTP	Actual Construction NTP	Projected Substantial Completion	Actual Substantial Completion	Project Closeout
PHASE 2 PROJECTS														
233	Adams, Nathan ES	01	JACOBS										11/7/2011	
972	Administrative Building	09	AECOM									5/28/2012		
065	Anderson, Pearl C. MS	09	JACOBS									TBD		
104	Anderson, William M. ES	04	PARSONS										9/30/2011	
042	Atwell, William Hawley Law Academy	06	PARSONS									3/30/2012		
352	Balch Springs MS	04	AECOM									7/16/2012		
980	Ballew, Forest E. Service Center	NA	AECOM									4/16/2012		
737	Berkeley, Dr. Marvin H. Human Resources Building	09	AECOM										12/15/2011	
109	Blair, W. A. ES	09	JACOBS									5/18/2012		
111	Bonham, James B. ES	08	PARSONS										12/28/2011	
117	Burleson, Rufus C. ES	09	JACOBS										1/12/2012	
119	Cabell, William L. ES	01	JACOBS										11/22/2011	
247	Callejo, Adelfa Botello ES	04	AECOM									7/16/2012		
121	Carpenter, John W. ES	06	AECOM									8/2/2012		
023	Carter, David W. HS	06	PARSONS									3/31/2012		
044	Cary, Edward H. MS	01	JACOBS									4/23/2012		
281	Chavez, Cesar Learning Center	08	JACOBS										12/14/2011	
127	City Park HS	09	PARSONS										11/15/2011	
045	Comstock, E. B. MS	09	JACOBS									3/30/2012		
136	Donald, L.O. ES	07	AECOM										1/27/2012	
266	Douglass, Frederick ES	09	JACOBS										12/14/2011	
139	Dunbar, Paul L. Learning Center	09	PARSONS										12/2/2011	
140	Earhart, Amelia ES	05	PARSONS									3/28/2012		
074	Edison, Thomas A. Learning Center	05	PARSONS									3/29/2012		
142	Ervin, J.N. ES	05	PARSONS									4/15/2012		
143	Fannin, James W. ES	08	JACOBS									TBD		
046	Florence, Fred F. MS	04	PARSONS										12/1/2011	
280	Frank, Anne ES	01	JACOBS										11/8/2011	
146	Frazier, Julia C. ES	09	PARSONS									TBD		
027	Fridia Jr., Otto M. Alternative High School	09	AECOM							TBD		TBD		
148	Gooch, Tom C. ES	01	JACOBS										11/10/2011	
049	Greiner, W.E. Exploratory Arts Academy	07	AECOM									3/25/2012		
149	Hall, Lenore Kirk ES	07	AECOM									5/23/2012		
981	Haskell Building	09	AECOM									4/16/2012		
157	Hogg, James S. ES	07	PARSONS									3/29/2012		
100	Holmes Jr., Zan Wesley MS	06	AECOM									4/19/2012		
158	Hooe, Lida ES	07	AECOM									5/23/2012		
160	Houston, Sam ES	08	JACOBS									3/29/2012		
063	Hulcy, D.A. MS	06	PARSONS									3/29/2012		
161	Ireland, John ES	09	JACOBS									4/30/2012		
061	Jackson, Maynard H. MS	05	JACOBS										11/18/2011	
007	Jefferson, Thomas HS	01	JACOBS									5/4/2012		
163	Johnston, Albert Sidney ES	05	AECOM									2/25/2012	2/28/2012	
164	Jones, Anson ES	07	AECOM									2/25/2012	2/23/2012	
133	Jordan, Barbara ES	06	AECOM									8/2/2012		
268	Kennedy, John F. ES	08	PARSONS										12/1/2011	
128	King Jr., Martin Luther ES	07	AECOM							TBD		TBD		



2008 Dallas ISD Bond Program
Exhibit A - Target Milestones - Phase 2
February 2012

Org No.	Project Name	Trustee District	Program Manager	Pre-Design (STB)	Schematic Design	Design Development	Construction Documents	Procurement - 1st Bid Ad	CSP Approval by Board	Estimated Construction NTP	Actual Construction NTP	Projected Substantial Completion	Actual Substantial Completion	Project Closeout
PHASE 2 PROJECTS														
167	Kleberg ES	04	PARSONS										10/19/2011	
173	Lanier, Sidney Expressive Art Vanguard	07	AECOM										1/27/2012	
009	Lincoln Humanities/Communications Magnet	09	AECOM									4/27/2012		
053	Long, J.L. MS	09	PARSONS									6/15/2012		
073	Longfellow, Henry W. Career Exploration Academy	02	AECOM									2/25/2012	2/29/2012	
032	Madison, James HS	09	AECOM									4/27/2012		
054	Marsh, Thomas C. MS	01	JACOBS										11/22/2011	
264	McNair, Ronald E. ES	06	JACOBS										9/26/2011	2/23/2012
184	Milam, Ben ES	02	PARSONS									3/29/2012		
004	Multiple Careers Magnet Center	08	PARSONS									4/30/2012		
024	North Dallas HS	02	JACOBS									6/30/2012		
190	Peabody, George ES	07	AECOM									5/23/2012		
191	Pease, Elisha M. ES	05	PARSONS									4/15/2012		
192	Peeler, John F. ES	07	AECOM										1/9/2012	
012	Pinkston, L.G. HS	07	PARSONS									5/31/2012		
733	Purchasing Center	09	JACOBS										8/5/2011	12/15/2011
035	Rangel, Irma Lerma Young Women's Leadership Sch	09	AECOM									4/27/2012		
196	Ray, J.W. Learning Center	09	JACOBS									3/2/2012		
197	Reagan, John H. ES	07	PARSONS									3/29/2012		
200	Rhoads, Joseph J. ES	09	JACOBS										1/13/2012	
201	Rice, Charles Learning Center	09	JACOBS									3/2/2012		
353	Richards, Ann MS	04	AECOM									7/16/2012		
013	Roosevelt, Franklin D. HS	05	AECOM									3/25/2012		
204	Rosemont ES	07	AECOM										1/9/2012	
244	Seagoville North ES	04	PARSONS									6/30/2012		
016	South Oak Cliff HS	05	PARSONS									3/21/2012		
058	Spence, Alex W. MS	08	PARSONS									3/28/2012		
263	Starks, J.P. Math, Science, and Technology Vanguard	05	AECOM										1/26/2012	
210	Stemmons, Leslie A. ES	06	AECOM									11/16/2012		
211	Stevens Park ES	07	AECOM									2/27/2012	2/28/2012	
059	Stockard, L.V. MS	06	AECOM									5/23/2012		
950	Student Support Services Center	NA	PARSONS										12/6/2011	
018	Sunset HS	07	PARSONS									5/31/2012		
214	Thompson, H. S. Learning Center	09	JACOBS									TBD		
215	Thornton, Robert L. ES	06	JACOBS										11/18/2011	
216	Titche, Edward ES	04	PARSONS										11/16/2011	
219	Turner, Adelle	06	JACOBS										11/18/2011	
224	Walnut Hill ES	01	JACOBS									4/23/2012		
226	Weiss, Martin ES	06	JACOBS										11/18/2011	
021	White, W.T. HS	01	AECOM									4/20/2012		
022	Wilson, Woodrow HS	09	PARSONS									8/15/2012		
131	Zaragoza, Ignacio ES	08	JACOBS										12/14/2011	



2008 Dallas ISD Bond Program

Exhibit A - Target Milestones - Phase 3

February 2012

Org No.	Project Name	Trustee District	Program Manager	Pre-Design (STB)	Schematic Design	Design Development	Construction Documents	Procurement - 1st Bid Ad	CSP Approval by Board	Estimated Construction NTP
PHASE 3 PROJECTS										
103	Allen, Gabe P. Charter School	07	AECOM				3/19/2012	4/1/2012	6/28/2012	8/17/2012
106	Arlington Park Community Learning Center	08	JACOBS	TBD	TBD	TBD	TBD	TBD	TBD	TBD
108	Bayles ES	03	AECOM			3/1/2012	5/29/2012	6/10/2012	8/23/2012	10/12/2012
962	Beckley Building	06	AECOM				4/17/2012	4/29/2012	8/23/2012	10/12/2012
274	Bethune, Mary Mcleod ES	07	PARSONS			3/8/2012	3/15/2012	3/25/2012	6/28/2012	8/17/2012
112	Bowie, James ES	07	PARSONS		3/5/2012	3/26/2012	4/2/2012	3/4/2012	5/24/2012	7/13/2012
043	Browne, T.W. MS	06	AECOM				4/17/2012	4/29/2012	8/23/2012	10/12/2012
116	Burnet, David G. ES	08	AECOM						5/24/2012	7/13/2012
125	Casa View ES	03	PARSONS				3/16/2012	3/13/2012	5/24/2012	7/13/2012
126	Central ES	04	JACOBS				3/1/2012	3/4/2012	5/24/2012	7/13/2012
236	Cochran, Nancy J. ES	07	PARSONS			3/8/2012	3/15/2012	3/25/2012	6/28/2012	8/17/2012
129	Conner, S.S. ES	03	AECOM				5/29/2012	6/10/2012	8/23/2012	10/12/2012
276	Cuellar Sr., Gilbert ES	04	PARSONS						4/26/2012	6/15/2012
062	Dade, Billy Earl MS	09	PARSONS						4/26/2012	6/15/2012
041	Ewell, Yvonne A. Townview Center	05	PARSONS		3/5/2012	3/26/2012	4/2/2012	3/4/2012	5/24/2012	7/13/2012
147	Gill, Charles A. ES	03	PARSONS				3/16/2012	3/13/2012	5/24/2012	7/13/2012
269	Hernandez, Onesimo ES	08	JACOBS	3/16/2012	3/30/2012	4/17/2012	6/4/2012	6/17/2012	9/27/2012	11/16/2012
050	Hill, Robert T. MS	03	PARSONS					3/4/2012	5/24/2012	7/13/2012
178	Holland, H.I. Elementary School at Lisbon ES	05	JACOBS				3/23/2012	4/1/2012	6/28/2012	8/17/2012
275	Kahn, Louise Wolff ES	07	AECOM				3/26/2012	4/8/2012	6/28/2012	8/17/2012
008	Kimball, Justin F. HS	06	AECOM				4/17/2012	4/29/2012	8/23/2012	10/12/2012
168	Knight, Obadiah ES	08	JACOBS	3/16/2012	3/30/2012	4/17/2012	6/4/2012	6/17/2012	9/27/2012	11/16/2012
183	Marsalis, Thomas L. ES	06	JACOBS						4/26/2012	6/15/2012
265	Martinez, Eladio R. Learning Center	05	AECOM				3/19/2012	4/1/2012	6/28/2012	8/17/2012
107	May, Jose "Joe" ES	01	PARSONS	TBD	TBD	TBD	TBD	TBD	TBD	TBD
283	Medrano, Esperanza "Hope" ES	08	JACOBS	3/16/2012	3/30/2012	4/17/2012	6/4/2012	6/17/2012	9/27/2012	11/16/2012
005	Molina, Moises E. HS	07	PARSONS			3/8/2012	3/15/2012	3/25/2012	6/28/2012	8/17/2012
272	Moreno, Maria ES	06	PARSONS			3/8/2012	3/15/2012	3/25/2012	6/28/2012	8/17/2012
003	New Tech HS at A. Maceo Smith HS	05	JACOBS						3/22/2012	5/11/2012
189	Oliver, Clara ES	05	JACOBS				3/23/2012	4/1/2012	6/28/2012	8/17/2012
958	Pegasus Complex	09	JACOBS				3/6/2012	3/11/2012	5/24/2012	7/13/2012
273	Pleasant Grove ES	04	PARSONS						4/26/2012	6/15/2012
068	Quintanilla Sr., Raúl MS	07	AECOM				3/26/2012	4/8/2012	6/28/2012	8/17/2012
199	Reinhardt ES	03	AECOM			3/1/2012	5/29/2012	6/10/2012	8/23/2012	10/12/2012
303	Richardson, Thelma Elizabeth Page ES	09	PARSONS						3/22/2012	5/11/2012
202	Roberts, Oran M. ES	09	JACOBS						4/26/2012	6/15/2012
271	Saldivar, Julian T. ES	08	AECOM						4/26/2012	6/15/2012
208	Seagoville ES	04	JACOBS				3/1/2012	3/4/2012	5/24/2012	7/13/2012
069	Seagoville MS	04	JACOBS				3/1/2012	3/4/2012	5/24/2012	7/13/2012
277	Tolbert, Thomas ES	06	PARSONS			3/8/2012	3/15/2012	3/25/2012	6/28/2012	8/17/2012
217	Travis, William B. ES	09	JACOBS				3/6/2012	3/11/2012	5/24/2012	7/13/2012
218	Truett, George W. ES	09	AECOM			TBD	TBD	TBD	TBD	TBD
